| ID | Name | Duration | Start | Finish |
|---|---|---|---|---|
| 1 | **OWNER'S PRELIMINARY MILESTONE SCHEDULE** | 0 days | Thu 8/1/19 | Thu 8/1/19 |
| 2 | CAPITAL CONSTRAINTS | 3287 days | Thu 8/1/19 | Fri 7/16/32 |
| 15 | JPS BOARD MEETINGS | 3274 days | Thu 8/8/19 | Thu 7/8/32 |
| 172 | PROGRAM MANAGER SELECTION | 116 days | Tue 9/17/19 | Wed 3/11/20 |
| 213 | STRATEGIC PLAN UPDATE | 193 days | Thu 3/12/20 | Tue 12/15/20 |
| 242 | CONSTRUCTION MANAGER SELECTION | 163 days | Fri 10/23/20 | Thu 6/24/21 |
| 272 | PHASED CONSTRUCTION COST ESTIMATES/DESIGN ASSIST MEETINGS | 2054 days | Fri 6/25/21 | Tue 8/14/29 |
| 381 | MANAGEMENT AND FINANCIAL AUDITOR SELECTION | 68 days | Thu 3/12/20 | Tue 6/16/20 |
| 392 | SURVEYOR SELECTION - TOPO & U.G. UTILITIES | 68 days | Thu 3/12/20 | Tue 6/16/20 |
| 403 | SURVEYING ACTIVITIES - TOPO & U.G. UTILITIES | 84 days | Wed 6/17/20 | Wed 10/14/20 |
| 413 | GEOTECH ENGINEER SELECTION - ALL PROJECTS | 68 days | Thu 3/12/20 | Tue 6/16/20 |
| 424 | GEOTECHNICAL ACTIVITIES | 80 days | Wed 6/17/20 | Thu 10/8/20 |
| 434 | MATERIALS TESTING AGENT SELECTION | 68 days | Thu 3/12/20 | Tue 6/16/20 |
| 445 | MATERIALS TESTING ACTIVITIES | 2750 days | Thu 9/30/21 | Fri 7/16/32 |
| 447 | A/E SELECTION - ALL NEW MEDICAL HOME PROJECTS | 35 days | Tue 12/15/20 | Fri 2/12/21 |
| 459 | NEW MEDICAL HOME 1 SITE SELECTION | 73 days | Thu 3/12/20 | Tue 6/23/20 |
| 463 | NEW MEDICAL HOME 1 DESIGN | 163 days | Mon 2/15/21 | Mon 10/4/21 |
| 472 | NEW MEDICAL HOME 1 CONSTRUCTION | 338 days | Sat 1/1/22 | Tue 5/9/23 |
| 480 | NEW MEDICAL HOME 2 SITE SELECTION | 73 days | Thu 3/12/20 | Tue 6/23/20 |
| 484 | NEW MEDICAL HOME 2 DESIGN | 133 days | Mon 5/10/21 | Wed 11/17/21 |
| 490 | NEW MEDICAL HOME 2 CONSTRUCTION | 338 days | Sat 1/1/22 | Tue 5/9/23 |
| 498 | NEW MEDICAL HOME 3 SITE SELECTION | 73 days | Wed 1/1/25 | Tue 4/15/25 |
| 503 | NEW MEDICAL HOME 3 DESIGN | 133 days | Thu 1/1/26 | Mon 7/6/26 |
| 510 | NEW MEDICAL HOME 3 CONSTRUCTION | 338 days | Fri 1/1/27 | Tue 4/18/28 |
| 518 | NEW MEDICAL HOME 4 SITE SELECTION | 73 days | Thu 1/1/26 | Mon 4/13/26 |
| 523 | NEW MEDICAL HOME 4 DESIGN | 133 days | Fri 1/1/27 | Tue 7/6/27 |
| 530 | NEW MEDICAL HOME 4 CONSTRUCTION | 338 days | Sat 1/1/28 | Wed 4/18/29 |
| 538 | INTERIM SURFACE PARKING LOT(S) SITE SELECTION | 72 days | Wed 3/11/20 | Mon 6/22/20 |
| 543 | A/E SELECTION - ALL PARKING PROJECTS | 93 days | Wed 12/16/20 | Wed 5/5/21 |
| 554 | INTERIM SURFACE PARKING LOT(S) DESIGN | 102 days | Thu 5/6/21 | Wed 9/29/21 |
| 565 | INTERIM SURFACE PARKING LOT(S) CONSTRUCTION | 100 days | Sat 1/1/22 | Mon 5/23/22 |
| 572 | BEHAVIORAL TOWER STRUCTURED PARKING DESIGN | 159 days | Fri 6/18/21 | Mon 2/14/22 |
| 581 | GMP 1 & PROGRAM CONTROL ESTIMATE - BEHAVIORAL TOWER STRUCTURED PA | 24 days | Mon 1/31/22 | Fri 3/4/22 |
| 587 | BEHAVIOR TOWER STRUCTURED PARKING CONSTRUCTION | 280 days | Tue 5/24/22 | Tue 7/11/23 |
| 593 | A/E SELECTION - ALL BEHAVIORAL PROJECTS | 93 days | Wed 12/16/20 | Wed 5/5/21 |
| 604 | WEST CENTRAL PLANT UPGRADES DESIGN | 197 days | Thu 5/6/21 | Thu 2/24/22 |
| 613 | GMP - WEST CENTRAL PLANT UPGRADES: PREPARATION AND BOARD APPROVA | 24 days | Thu 2/24/22 | Wed 3/30/22 |
| 619 | WEST CENTRAL PLANT UPGRADES CONSTRUCTION | 271 days | Thu 3/31/22 | Tue 5/2/23 |
| 626 | NEW PSYCHIATRIC EMERGENCY CENTER DESIGN | 174 days | Thu 5/6/21 | Mon 1/24/22 |
| 635 | GMP - NEW PSYCHIATRIC EMERGENCY CENTER: PREPARATION AND BOARD APP | 24 days | Fri 1/7/22 | Fri 2/11/22 |
| 641 | NEW PSYCHIATRIC EMERGENCY CENTER CONSTRUCTION | 424 days | Tue 1/25/22 | Tue 10/3/23 |
| 648 | NEW BEHAVIORAL PATIENT TOWER DESIGN | 351 days | Thu 5/6/21 | Mon 10/3/22 |
| 657 | GMP - NEW BEHAVIORAL PATIENT TOWER: PREPARATION AND BOARD APPROV | 24 days | Mon 9/12/22 | Fri 10/14/22 |
| 663 | NEW BEHAVIORAL PATIENT TOWER CONSTRUCTION | 609 days | Tue 10/4/22 | Thu 3/27/25 |
| 670 | A/E SELECTION - PATIENT CARE CENTER (PCC) | 93 days | Wed 12/16/20 | Wed 5/5/21 |
| 681 | EAST CENTRAL PLANT EXPANSION DESIGN | 167 days | Thu 5/6/21 | Wed 1/12/22 |
| 690 | GMP - EAST CENTRAL PLANT EXPANSION: PREPARATION AND BOARD APPROVA | 24 days | Wed 1/12/22 | Wed 2/16/22 |
| 696 | EAST CENTRAL PLANT CONSTRUCTION | 271 days | Thu 2/17/22 | Tue 3/21/23 |
| 703 | MORPHY STREET STAFF GARAGE REPLACEMENT PHASE 1 & 2 DESIGN | 167 days | Thu 5/6/21 | Wed 1/12/22 |
| 712 | GMP - MORPHY STREET STAFF GARAGE REPLACEMENT PHASE 1: PREPARATION | 24 days | Tue 12/21/21 | Wed 2/2/22 |
| 718 | MORPHY STREET STAFF GARAGE REPLACEMENT PHASE 1 CONSTRUCTION | 369 days | Thu 2/3/22 | Wed 7/26/23 |
| 725 | PATIENT CARE CENTER & RELATED STRUCTURED PARKING DESIGN | 296 days | Thu 5/6/21 | Fri 7/15/22 |
| 734 | GMP - PATIENT CARE CENTER & RELATED STRUCTURED PARKING: PREPARATIO | 24 days | Thu 6/30/22 | Thu 8/4/22 |
| 740 | PATIENT CARE CENTER & RELATED STRUCTURED PARKING CONSTRUCTION | 504 days | Mon 7/18/22 | Tue 7/30/24 |
| 747 | A/E SELECTION - NEW PATIENT TOWER | 93 days | Mon 1/1/24 | Fri 5/10/24 |
| 759 | LOADING DOCK RELOCATION DESIGN | 197 days | Thu 5/6/21 | Thu 2/24/22 |
| 768 | GMP - LOADING DOCK RELOCATION: PREPARATION AND BOARD APPROVAL | 24 days | Thu 2/24/22 | Wed 3/30/22 |
| 774 | LOADING DOCK RELOCATION CONSTRUCTION | 271 days | Thu 3/31/22 | Tue 5/2/23 |
| 781 | GMP - MORPHY STREET STAFF GARAGE REPLACEMENT PHASE 2: PREPARATION | 24 days | Sat 1/1/28 | Thu 2/3/28 |
| 788 | MORPHY STREET STAFF GARAGE REPLACEMENT PHASE 2 CONSTRUCTION | 444 days | Fri 2/4/28 | Wed 10/17/29 |
| 796 | NEW INPATIENT TOWER DESIGN | 409 days? | Thu 1/2/25 | Tue 8/18/26 |
| 806 | GMP - NEW INPATIENT TOWER: PREPARATION AND BOARD APPROVAL | 24 days | Mon 8/3/26 | Fri 9/4/26 |
| 812 | NEW INPATIENT TOWER CONSTRUCTION | 756 days | Fri 1/1/27 | Fri 11/23/29 |
| 820 | A/E SELECTION - BACKFILL RENOVATIONS | 93 days | Sat 1/1/28 | Wed 5/10/28 |
| 832 | BACKFILL RENOVATIONS DESIGN | 336 days | Thu 5/11/28 | Thu 8/23/29 |
| 841 | GMP - BACKFILL RENOVATIONS: PREPARATION AND BOARD APPROVAL | 24 days | Wed 8/8/29 | Tue 9/11/29 |
| 847 | BACKFILL RENOVATIONS CONSTRUCTION | 756 days | Thu 8/23/29 | Fri 7/16/32 |
| 855 | QUALITY CONTROL | 3136 days | Thu 3/12/20 | Wed 7/14/32 |
| 1005 | AUTHORITIES HAVING JURISDICTION COORDINATION | 3113 days | Wed 4/1/20 | Thu 7/1/32 |
| 1206 | FINANCING | 2362 days | Thu 8/1/19 | Mon 1/1/29 |
| 1237 | OFF SITE UTILITIES DESIGN | 141 days | Thu 5/6/21 | Mon 11/29/21 |
| 1242 | OFF SITE UTILITIES CONSTRUCTION | 415 days | Tue 11/30/21 | Thu 8/3/23 |

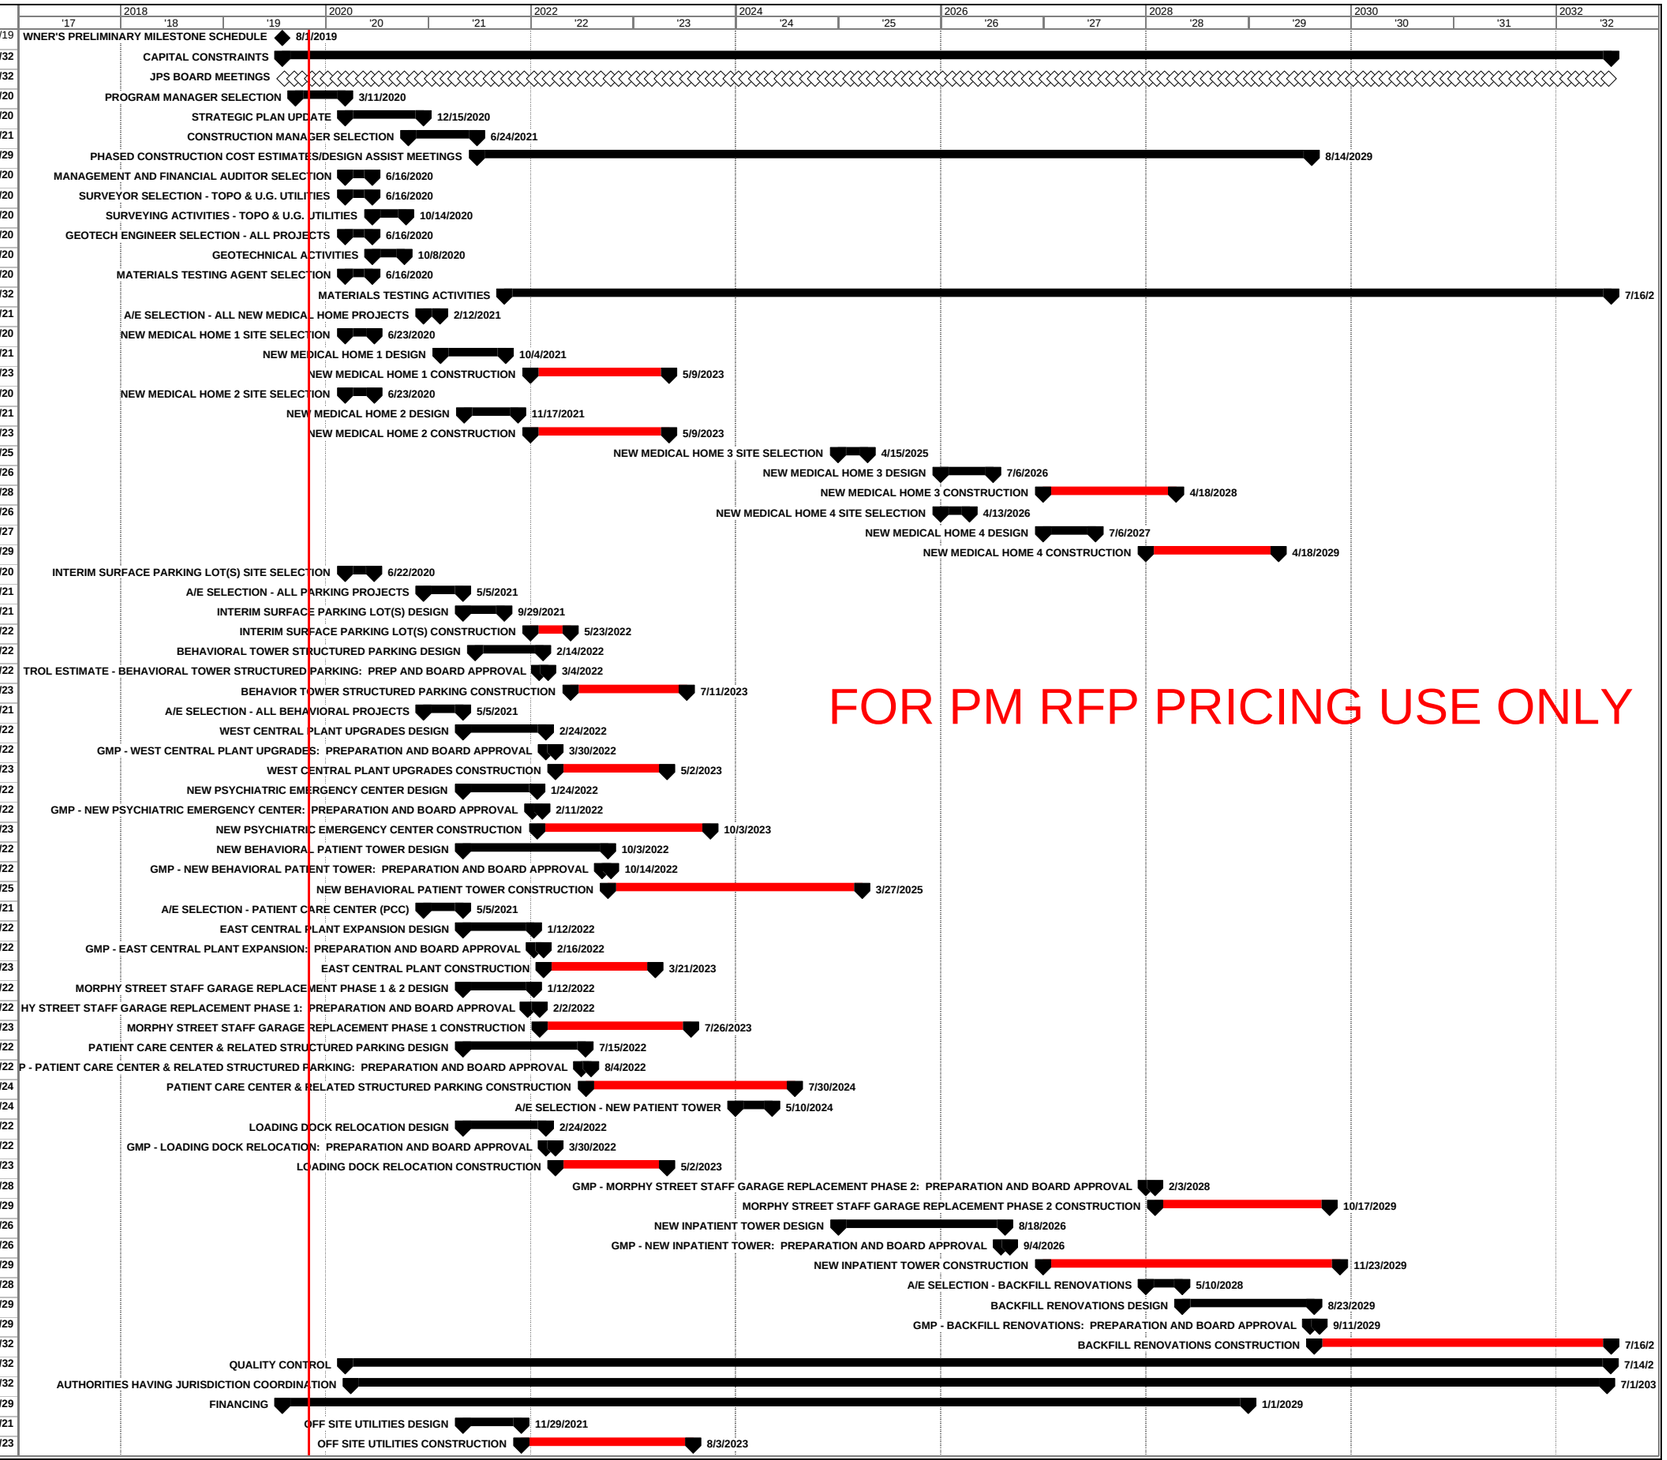


FOR PM RFP PRICING USE ONLY

Project: JPS Milestone Schedule S5.V1 191030 1600
Date: Thu 10/31/19

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
